



U.S. Department of Energy
Office of Civilian Radioactive Waste Management



Yucca Mountain Project Status - Exhibits

Presented to:

**Nuclear Waste Technical Review Board Panel on the
Engineered System**

Presented by:

W. John Arthur, III

Deputy Director


Office of Repository Development

U.S. Department of Energy

January 20, 2004

Las Vegas, Nevada


Summary Schedule to License Application Submittal

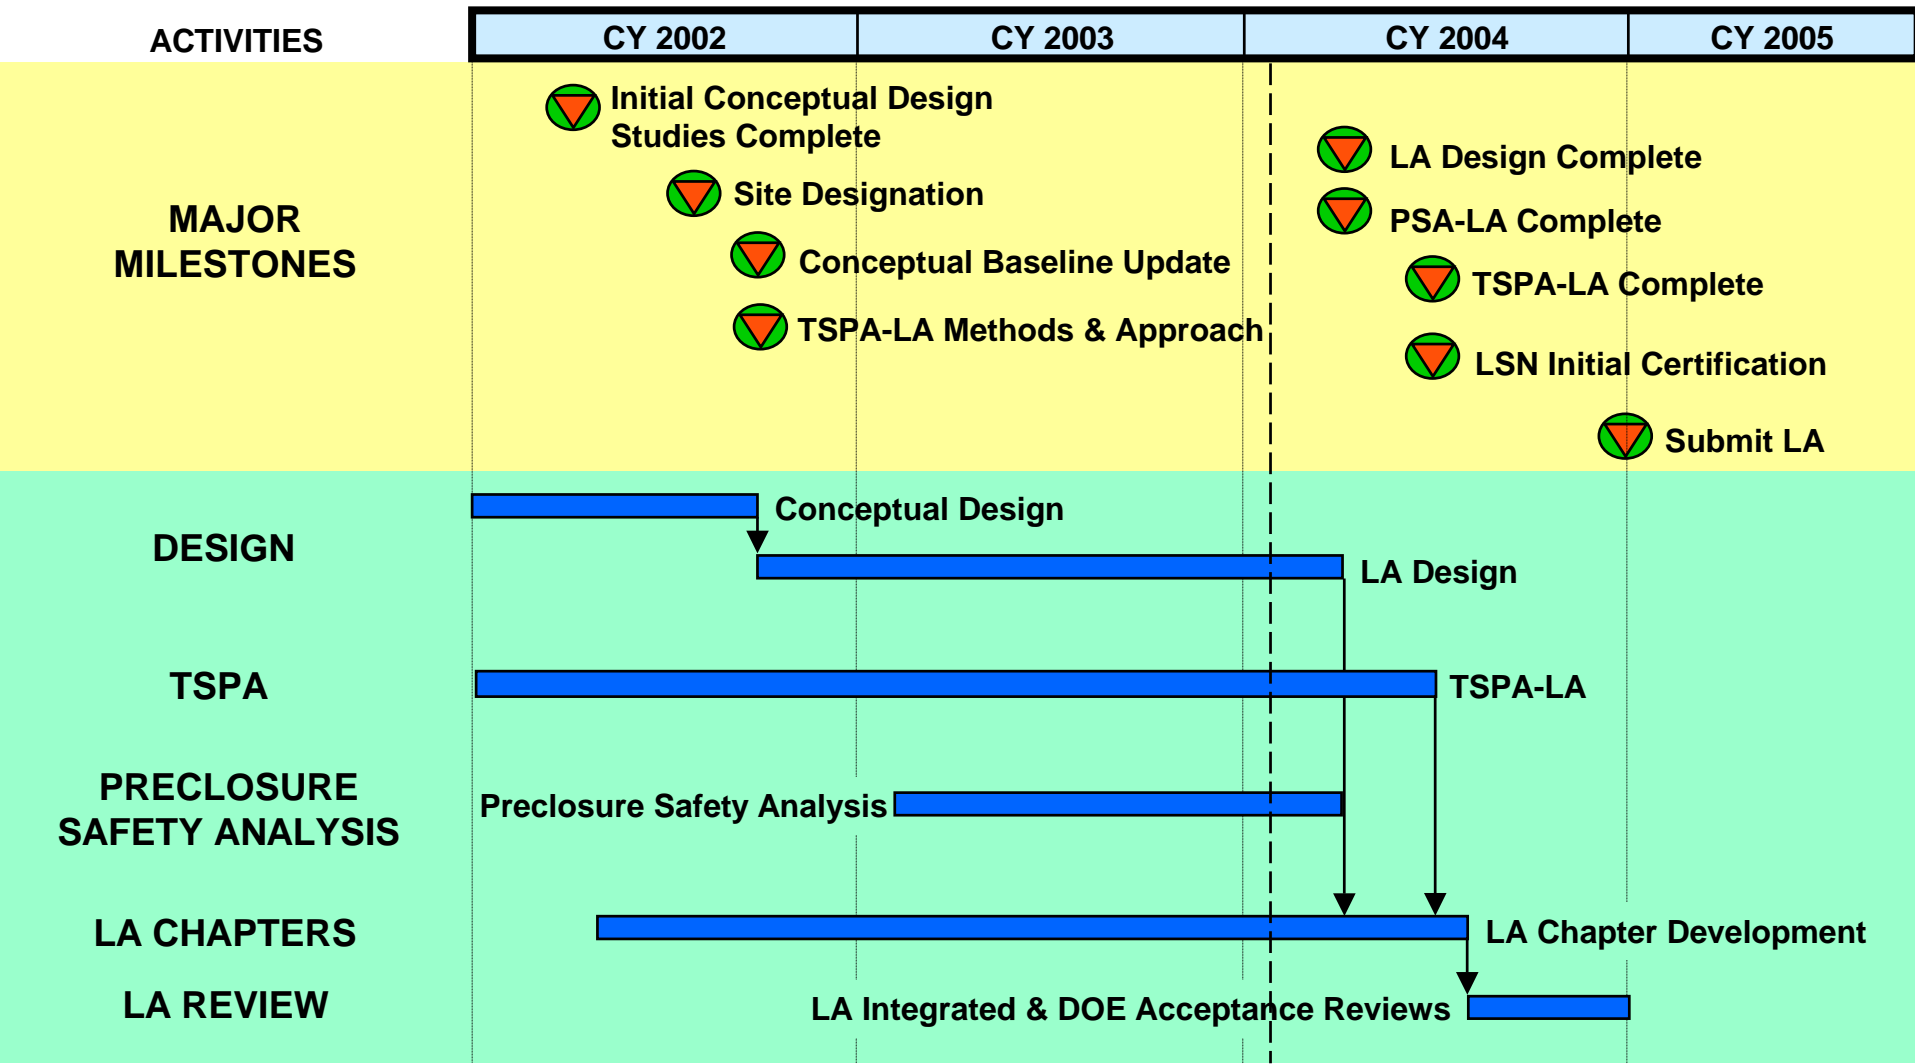

CY = Calendar Year



Potential Nevada Rail Corridors

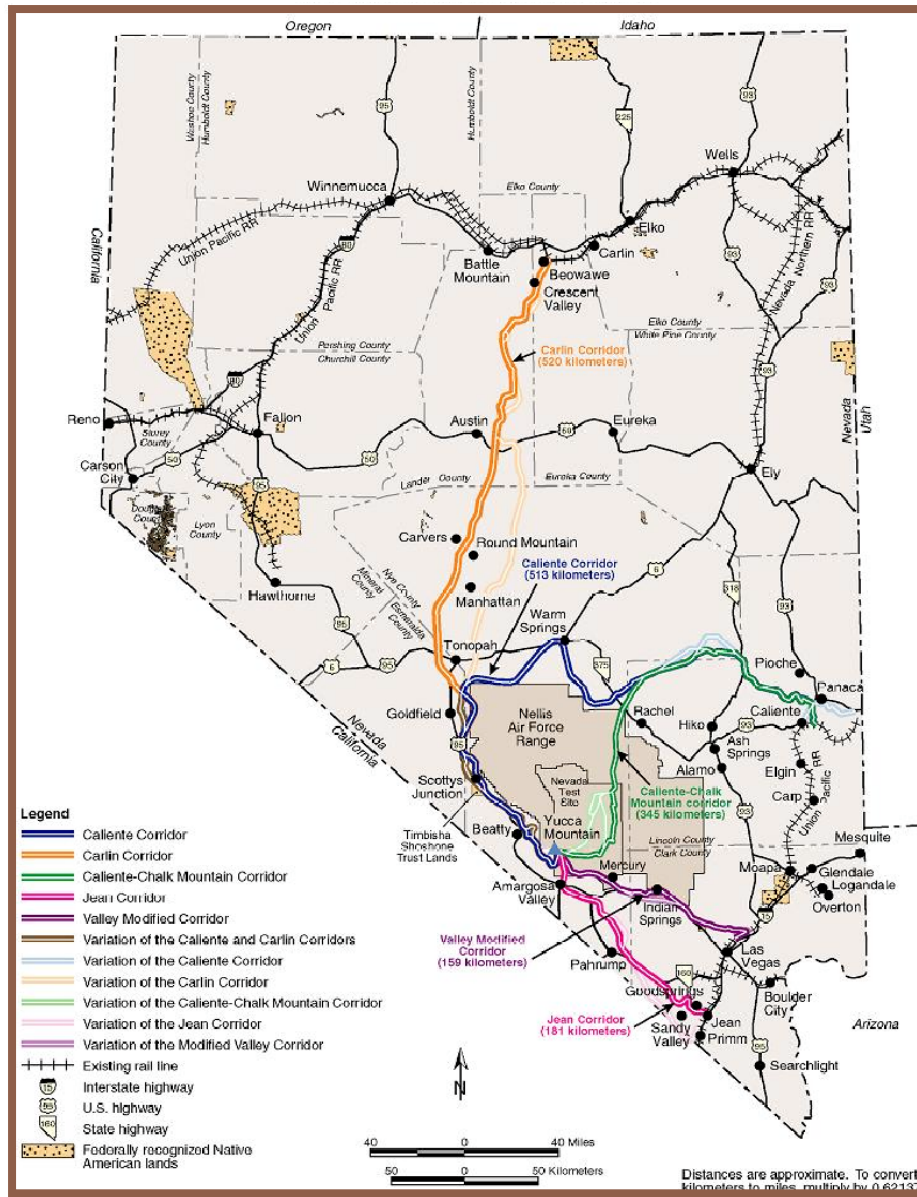

Reprinted from Final Environmental Impact Statement



Management Assessment of Progress Towards License Application


<u>COMPONENT</u>	<u>% COMPLETE</u>	<u>% PLANNED</u>	<u>WEIGHT</u>
KTI Agreements addressed	70%	70%	10%
LA Document	14%	14%	20%
Preclosure Safety Assessment	45%	45%	10%
TSPA-LA	73%	81%	30%
Design	<u>56%</u>	<u>59%</u>	<u>30%</u>
TOTAL % COMPLETE	53%	56%	100%

Data through 12/31/03



Scheduled Key Technical Issue Submittals Versus Actual

KTI Agreement Response Status

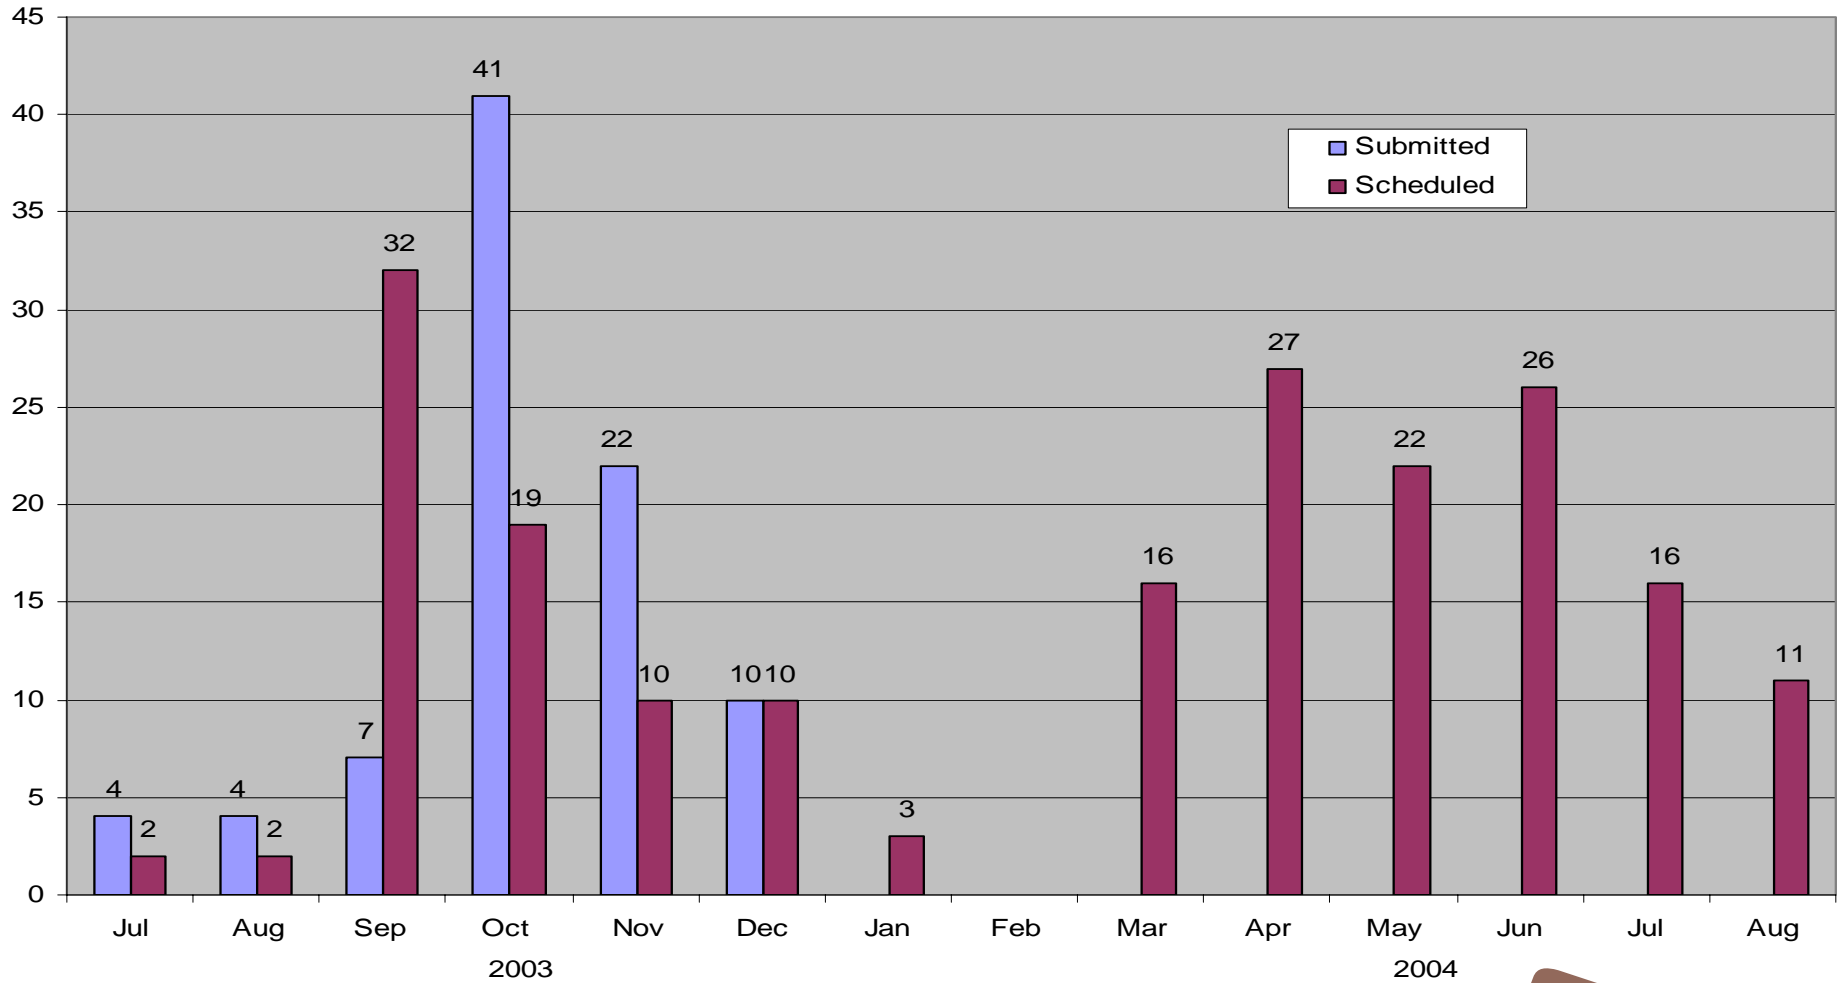

Data as of 12/31/03

